Corner B+C:
Section 31-97-12
As referred to in
Engr. Tie Book.

>

Chickasaw Co. Recorder
Cindy Messersmith
**Fee Book 2007-1654**
08/17/2007 @0430PM
SCC SEC COR CERT
Book: Page: # Pages: 1
Total Fees: $7.00

*Herold - Reicks Surveying, 25 1/2 East Main Street, Suite 204, New Hampton, IA 50659, Ph. 641-394-2725*

# UNITED STATES PUBLIC LAND SURVEY CORNER CERTIFICATE

Land Survey Monuments situated in:
Section 31/~~32~~, Township 97 North, Range 12 West of the Fifth Principal Meridian,
Chickasaw County, Iowa. Previously recorded in 1.) Bk. 173, Pg. 51
in County Recorder's Office. 2.) Bk. 173, Pg. 50

(Show reason for preparing this certificate, the evidence and detailed procedures used in establishing the corner positions and monumentation found or placed.)

Monument Description and Remarks: W 1/4 Corner Section 32-97-12 & SW Corner Section 32-97-12, both previous Section Corner Monuments were covered over by an HMA resurfacing project, set MAG Nails w/ Stainless Steel Washers PLS 15525 at both Corners, filing a new Section Corner Certificate to indicate new monumentation of the Corners.

## PLAN - VIEW

(Show a minimum of three reference ties to durable physical objects, relevant monuments and physical conditions that will enable recovery of the corner.)

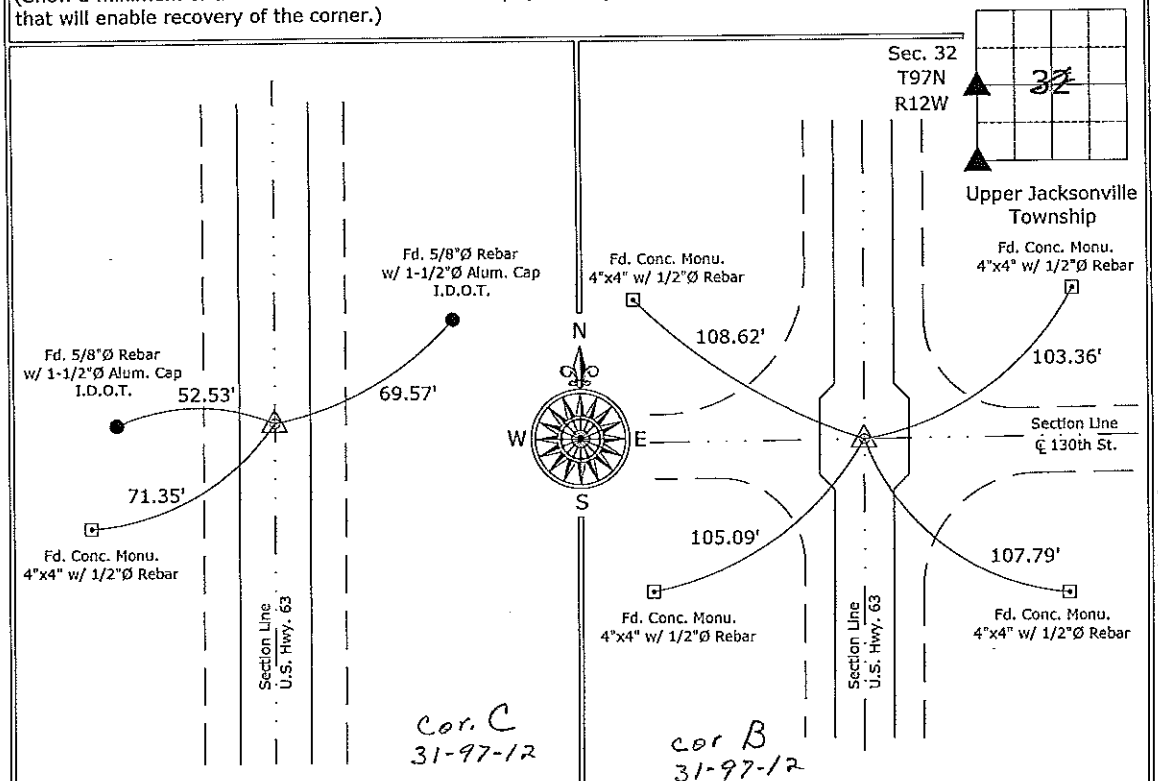


1.) W 1/4 Corner Section 32-97-12
Set MAG Nail w/ Stainless Steel Washer PLS 15525

2.) SW Corner Section 32-97-12
Set MAG Nail w/ Stainless Steel Washer PLS 15525

PROFESSIONAL LAND SURVEYOR
PAUL R. HEROLD
15525
IOWA

I hereby certify that this land surveying document was prepared and the related survey work was performed by me or under my direct personal supervision and that I am a duly licensed Land Surveyor under the laws of the State of Iowa.

Paul R. Herold 8-17-07
Paul R. Herold Date:
License number 15525
My license renewal date is December 31, 2008.
Sheets covered by this seal: Individual sheet only

List Corners to be Indexed

| Corners | Section | Twp. | Range |
|---|---|---|---|
| W 1/4 | 32 | 97 | 12 |
| SW | 32 | 97 | 12 |

Project Number:2007-082
FB: Chickasaw Co. 1, Pg. 34

File: S:_Projects\2007\2007-080-082\dwg\2007-080-082.dwg, 8/20/2007 9:15:03 AM
